

Newsletter May 2025

Dear Neighbours,

Welcome to our regular update on the 2 Aldermanbury development from Bovis. This regular newsletter will keep you up to date with the progress we have made, what we will be working on in the coming months, community events you can get involved with and how to get in touch.


Construction Update

Structural steel including all the roof top plant steels have been installed. Roof top pipework modules & air handling units have been delivered. Waterproofing finishes to the roof are progressing well. Cladding panels are now at Lv12, corners are up to Lv12 & balconies are ongoing & we are awaiting the plantroom rain screens.

We had a great result with our last Considerate Constructors Scheme visit & scored 45 out of 45, and look forward to the City of London judges for the "Chairman's award", the best project in the City of London.

Showers and changing facilities in basement 1 are now being tiled which sees a daily change in progress.

Looking ahead in May, cladding will be up to the roof, and we start to fit out the main reception space. We are now in our new welfare inside the building & this will allow the demolition of the old welfare facility which will ultimately form the developments retail units.

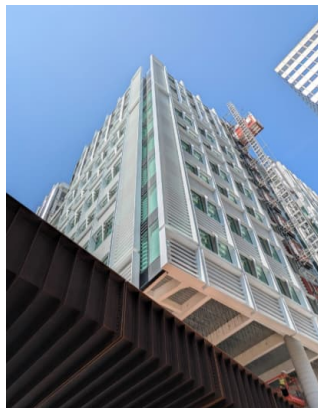

Working Hours

General working hours during this time will be:

Monday – Friday: 8am – 6pm

Saturday: 9am – 2pm

Contact Us

If you have any concerns or questions, the staff listed below will be available to help, including the 24-hour on-site security team in case of any urgent issues:

Alan Webster
Simon Ranauro
24hr Security

Construction Liaison & Logistics
Snr Project Manager

07876 718963
07849 838358
0208 826 4307

Alan.Webster@Bovis.com
Simon.Ranauro@Bovis.com
